


FY 15 SUMMER SHUTDOWN SCHEDULE (REV. 1.0)

*Bill Christie
For the STAR Collaboration
June 15, 2015*



BROOKHAVEN
NATIONAL LABORATORY
a passion for discovery

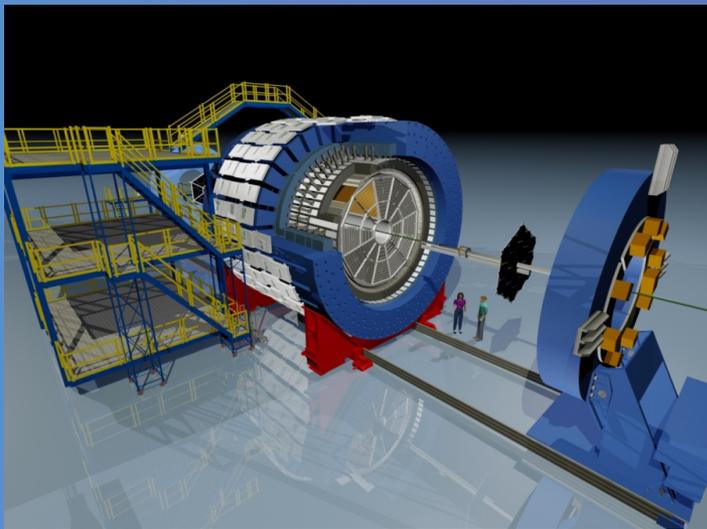

U.S. DEPARTMENT OF
ENERGY

Office of
Science

June						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22 Beam Ops. Cease ~ 8 am	23 Magnet Off	24 Remove W. BBC Gas Purge	25	26 Drain and Blow out Magnet Coils	27
	← TPC/HFT Cosmics →					
28	29	30				
	← Remove West Poletip & install Scaffolding →					
	← Remove E. BBC →					

Holidays and Observances: 21: Fathers' Day

July							
Sun	Mon	Tue	Wed	Thu	Fri	Sat	
			1	2	3	4	
			← Set up for PXL removal →				
5	6	7	8	9	10	11	
	← Remove N & S PXL assemblies & PXL platform →						
12	13	14	15	16	17	18	
	← Remove East Poletip and Install scaffolding →		← Remove failed BSMD Fee cards →				
19	20	21	22	23	24	25	
	Miscellaneous maintenance efforts expected to occur throughout July						
26	27	28	29	30	31		
Holidays and Observances: 3: 'Independence Day' observed, 4: Independence Day							

August						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1
2 RHIC Summer Sunday Open House	3 Miscellaneous maintenance efforts expected to occur throughout August	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

September						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1	2	3	4	5
Miscellaneous maintenance efforts expected to occur throughout September						
6	7	8	9	10	11	12
13	14	15	16	17	18	19
BEMC Maintenance work Both ends of STAR						
20	21	22	23	24	25	26
27	28	29	30			
Holidays and Observances: 7: Labor Day						

October

Sun	Mon	Tue	Wed	Thu	Fri	Sat
				1	2	3
Miscellaneous maintenance efforts expected to occur throughout August						
4	5	6	7	8	9	10
← BEMC Maintenance work Both ends of STAR →						
11	12	13	14	15	16	17
← →						
18	19	20	21	22	23	24
25	26	27	28	29	30	31

Holidays and Observances: 12: Columbus Day (Most regions), 31: Halloween


November

Sun	Mon	Tue	Wed	Thu	Fri	Sat
1	2	3	4	5	6	7
	← SGIS recertification and Fire alarm recertification →				Dress E. TPC face & Remove E. scaffolding	
8	9	10	11	12	13	14
	↔ Insert, attach, & hookup E. Poletip ↔	↔ Insert, attach, & hookup E. Poletip ↔		Install PXL platform		
15	16	17	18	19	20	21
	← Install & hook up N & S PXL assemblies →					
22	23	24	25	26	27	28
29	30					
	Dress W. TPC face & Remove W. scaffolding					

Holidays and Observances: 11: Veterans Day, 26: Thanksgiving Day

December						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1	2	3	4	5
		← Insert, attach, & Hookup West Poletip →		← EEMC maintenance →		
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		
			Fill and start Magnet H ₂ O system			
Holidays and Observances: 24: Christmas Eve, 25: Christmas Day, 26: Day After Christmas Day, 31: New Year's Eve						

January 2016

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
3	4	5	6	7	8	9
 Magnet checkout & Heat run, TPC HV check						 Install & light check BBCs
10	11	12	13	14	15	16
 Install & light check BBCs		STAR ready for Cosmic Ray testing				
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

Holidays and Observances: 1: New Year's Day, 18: Martin Luther King Day
