Core Facility Revitilization

Activity Name	Start	Finish
Milestone Level: L1	22-Feb-16	30-Nov-18
CD-0 Approve Mission Need	22-Feb-16	
CD-1 Approve Alternative Selection & Cost Range		30-Sep-16
CD-2/3A Approve Performance Balseline/Site Prep		31-May-18
CD-3 Approve Start of Construction		30-Nov-18
Milestone Level: L2	11-Dec-17	21-Jul-21
Award A/E Design Contract		11-Dec-17
Award CM/GC Pre-Constructin Services - Phase 1		31-Jan-18
Complete Preliminary Design (30% Document)		30-Apr-18
Complete Final Design (Bid Documents)		31-Oct-18
Start Construction - Issue NTP	03-Dec-18	
Construction Substantially Complete		29-May-20
CD-4 Approve Project Completeion		21-Jul-21*
Milestone Level: L3	01-Jun-18	03-Dec-18
Start Site Preparation Activities	01-Jun-18	
Award CM/GC Construction Services - Phase 2		03-Dec-18

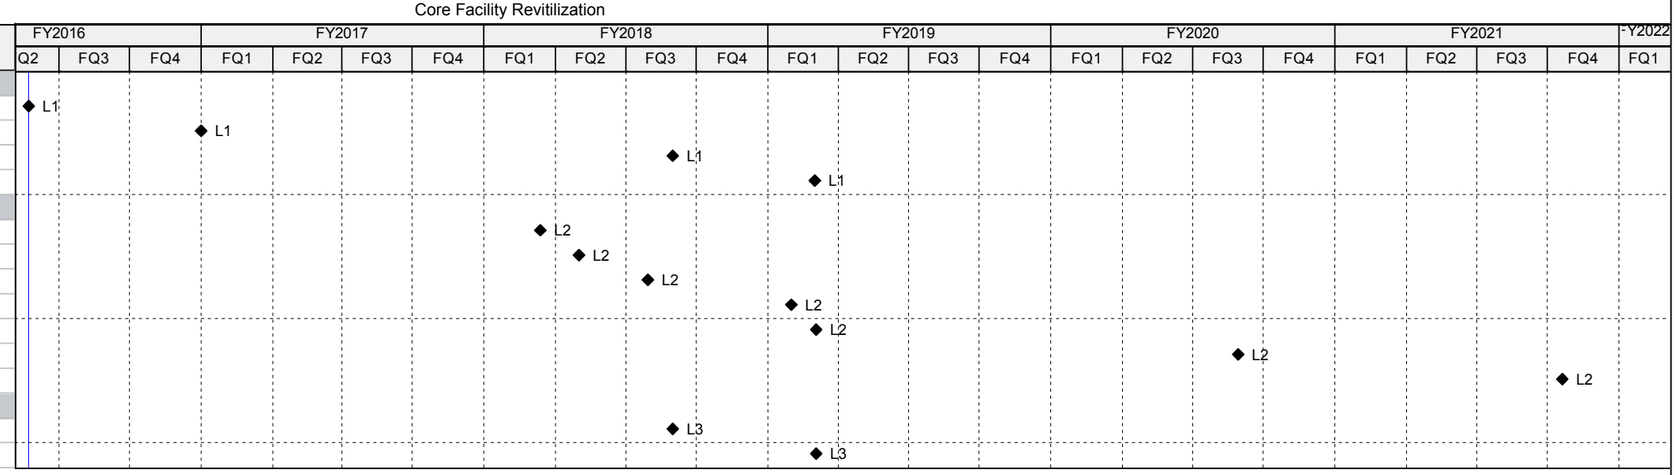

◆ Milestone

TASK filter: CFR Milestone.

Data Date: 22-Feb-16 Current Date: 01-Aug-16
