Core Facility Revitilization

Activity ID	Activity Name	Planned Duration	Start	Finish
1 CFR CD-1		1502d	01-Sep-15	01-Sep-21
1.M Milestones		1472d	01-Sep-15	21-Jul-21
MS4000	CD-4 Approve Project Completeion	0d		21-Jul-21*
MS3150	Construction Substantially Complete	0d		29-May-20
MS3100	Start Construction - Issue NTP	0d	03-Dec-18	
MS3050	Award CM/GC Construction Services - Phase 2	0d		03-Dec-18
MS3000	CD-3 Approve Start of Construction	0d		30-Nov-18
MS2300	Start Site Preparation Activities	0d	01-Jun-18	
MS2250	Complete Final Design (Bid Documents)	0d		31-Oct-18
MS2000	CD-2/3A Approve Performance Balseline/Site Prep	0d		31-May-18
MS1150	Complete Preliminary Design (30% Document)	0d		30-Apr-18
MS1100	Award CM/GC Pre-Constructin Services - Phase 1	0d		31-Jan-18
MS1050	Award A/E Design Contract	0d		11-Dec-17
MS1000	CD-1 Approve Alternative Selection & Cost Range	0d		30-Sep-16
MS0000	CD-0 Approve Mission Need	0d	01-Sep-15	
1.A Critical Decisions		1502d	01-Sep-15	01-Sep-21
1.A.01 CD-0		0d	01-Sep-15	01-Sep-15
1.A.02 CD-1		556d	07-Oct-15	29-Dec-17
1.A.3 CD-2/3A		105d	02-Jan-18	31-May-18
1.A.4 CD-3B		126d	01-Jun-18	30-Nov-18
1.A.5 CD-4		317d	01-Jun-20	01-Sep-21
1.B Procurement		480d	03-Jan-17	03-Dec-18
1.B.1 Procure A/E Services		171d	06-Apr-17	11-Dec-17
1.B.2 Procure CMGC Pre-Construction Services - Develop RFP		181d	03-Jan-17	20-Sep-17
1.B.3 Procure CMGC Construction		292d	02-Oct-17	03-Dec-18
1.B.4 Procure Facitlity Commissioning Agent		55d	02-Jan-18	21-Mar-18
1.01 Project Design and Engineering - Planning Packages		524d	03-Oct-16	05-Nov-18
1.01.01 A/E Preliminary and Final Design		212d	02-Jan-18	31-Oct-18
1.01.02 CMGC - Pre-Construction Services - Phase I		191d	02-Jan-18	02-Oct-18
1.01.03 Comminssioning Services - Pre-Construction Services		160d	22-Mar-18	05-Nov-18
1.01.04 Project Management - Pre-Construction Phase		231d	03-Oct-16	06-Sep-17
1.01.05 BNL/MPO Engineering Support - Pre-Construction Phase		231d	03-Oct-16	06-Sep-17
1.02 Construction - Planning Packages		585d	01-Jun-18	30-Sep-20
1.02.01 Site Prep/Long Lead Procurements		124d	01-Jun-18	28-Nov-18
1.02.02 Building Construction		373d	03-Dec-18	29-May-20
1.02.03 A/E Construction Administration Services		373d	03-Dec-18	29-May-20
1.02.04 Comminssioning - Construction Phase		388d	03-Dec-18	19-Jun-20
1.02.05 Project Management - Constrcuction Phase		585d	01-Jun-18	30-Sep-20
1.02.06 Project Support - Construction Phase		521d	01-Jun-18	30-Jun-20
1.03 Other project Costs (OPC)		1160d	07-Oct-15	29-May-20
1.03.01 Other Project Costs		1160d	07-Oct-15	29-May-20

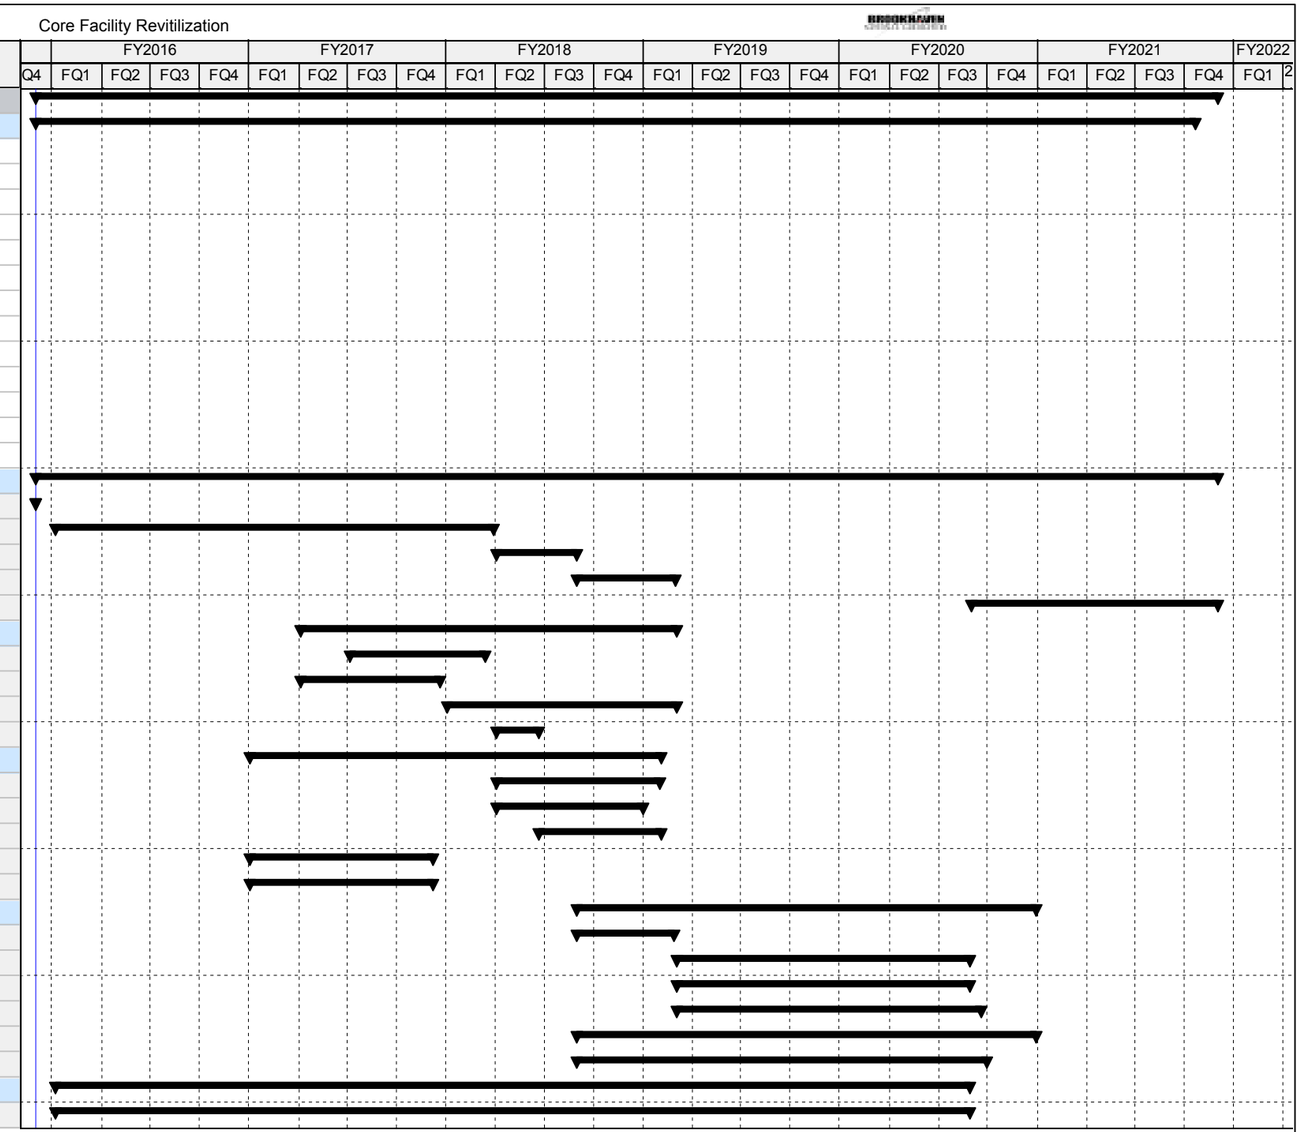

Summary

TASK filter: All Activities

Data Date: 01-Sep-15 Current Date: 04-Aug-16
